



















ID	% Complete	Task Name	Duration	Start	Finish	Preced	Resource Names	2nd Q Apr
1	31%	<b>Information Commons</b>	225 days?	Thu 5/21/09	Wed 3/31/10			
10	0%	Refresh Computers - wait on budget	24 days?	Tue 12/1/09	Fri 1/1/10		Louis,Andrew	
13	0%	Refresh Servers - waiting on budget	23 days?	Thu 10/1/09	Mon 11/2/09		Steve	
16	0%	January Ghosting	62 days?	Mon 11/2/09	Tue 1/26/10		Jackie Y	
24	0%	Windows 7 OS	53 days	Wed 12/30/09	Fri 3/12/10		Jackie Y,Steve	
27	0%	Ghost loaner laptops	43 days?	Mon 2/1/10	Wed 3/31/10		Louis,Andrew	
30	33%	<b>Staff Computers</b>	281 days?	Mon 5/4/09	Mon 5/31/10			
31	0%	Refresh Staff Computers - waiting on budget	60 days	Mon 3/1/10	Fri 5/21/10		David	
34	40%	Refresh Student Computers	60 days	Mon 3/1/10	Fri 5/21/10		Andrew	
36	10%	Implement Plan	40 days	Mon 3/29/10	Fri 5/21/10	35	Andrew	
37	28%	Plan for Windows 7 - wait for 7 to be out of beta (printservers,Forefront)	130 days	Wed 7/1/09	Tue 12/29/09		Andrew	
38	80%	Research	45 days	Wed 7/1/09	Tue 9/1/09		Andrew	
39	0%	Plan	25 days	Wed 9/2/09	Tue 10/6/09	38	Andrew	
40	0%	Test	60 days	Wed 10/7/09	Tue 12/29/09	39	Andrew	
41	25%	<b>Security Projects</b>	220 days	Wed 7/1/09	Tue 5/4/10		Jackie D	
42	25%	Create Plan	20 days	Wed 7/1/09	Tue 7/28/09		Jackie D	
43	25%	Implement Plan	200 days	Wed 7/29/09	Tue 5/4/10	42	Jackie D	
44	0%	UST refresh - not need	40 days	Tue 9/1/09	Mon 10/26/09			
48	0%	Switch to UA email and calendaring option - wait on UITS	51 days?	Thu 10/1/09	Thu 12/10/09		Jackie D	
55	86%	Upgrade Staff Memory	108 days	Wed 6/3/09	Fri 10/30/09		David,Andrew	
57	85%	Implement Plan	103 days	Wed 6/10/09	Fri 10/30/09	56		
58	0%	Upgrade to Windows 7 for Staff	21 days?	Mon 5/3/10	Mon 5/31/10		Andrew,Jackie Y	
62	0%	Support for alternative HW/SW w/ UST - Wait on UST	100 days	Mon 9/7/09	Fri 1/22/10		David,Louis	
66	98%	Research ghosting options - need gig to desktop	51 days?	Tue 9/1/09	Tue 11/10/09		Louis,Steve	
69	0%	Implement best option - none	1 day?	Tue 11/10/09	Tue 11/10/09	68		
70	71%	<b>Surplus process</b>	21 days?	Mon 9/14/09	Mon 10/12/09		Andrew	
72	50%	Get team input and then approval	10 days	Mon 9/28/09	Fri 10/9/09	71	XWING	
73	0%	Implement new process	1 day?	Mon 10/12/09	Mon 10/12/09	72	XWING	
74	53%	<b>Periferal Inventory</b>	126 days?	Mon 5/4/09	Mon 10/26/09		Louis	
79	0%	Have students check inventory	20 days	Tue 9/29/09	Mon 10/26/09	78	Louis	
80	26%	<b>Server Services</b>	220 days?	Wed 7/1/09	Tue 5/4/10			
81	0%	Refresh Linux Servers & Storage - wait for budget	40 days	Mon 10/5/09	Fri 11/27/09		Bob,Ann	
84	25%	Implement retirement of SAN	68 days	Wed 7/1/09	Fri 10/2/09		Jackie D,Bob	
86	0%	Implement Plan - Dependant on DCAP	30 days	Mon 8/24/09	Fri 10/2/09			
87	27%	<b>Security Vulnerability Scan</b>	220 days	Wed 7/1/09	Tue 5/4/10		Jackie D,Bob,Steve,Ann	










Project: XWING projects 0910 - Proj 2 Date: Tue 10/13/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	% Complete	Task Name	Duration	Start	Finish	Preced	Resource Names	2nd Q Apr
89	20%	Implement Plan	200 days	Wed 7/29/09	Tue 5/4/10	88		
93	8%	<b>IR move</b>	60 days	Wed 7/1/09	Tue 9/22/09		Bob	
94	15%	Work with IR group to Plan	30 days	Wed 7/1/09	Tue 8/11/09		Bob	
95	0%	Implement plan	30 days	Wed 8/12/09	Tue 9/22/09	94	Bob	
96	98%	<b>New Main website</b>	60 days	Wed 7/1/09	Tue 9/22/09		Bob	
98	95%	Implement plan	30 days	Wed 8/12/09	Tue 9/22/09	97	Bob	
99	0%	Possible Streaming Expansion	1 day?	Mon 8/3/09	Mon 8/3/09			
100	0%	<b>Video Technology Research</b>	65 days	Mon 2/1/10	Fri 4/30/10		David	
104	0%	<b>Test Cloud Computing</b>	147 days?	Thu 10/1/09	Fri 4/23/10		Bob	
105	2%	Create Plan	22 days?	Thu 10/1/09	Fri 10/30/09			
106	0%	Implement test	85 days?	Mon 11/2/09	Fri 2/26/10	105		
107	0%	Review findings	40 days	Mon 3/1/10	Fri 4/23/10	106		
108	14%	<b>Branch Computers</b>	192 days	Mon 6/15/09	Tue 3/9/10			
109	0%	Branch IC refresh - wait for budget	41 days	Tue 12/1/09	Tue 1/26/10		Ann,Jackie Y	
116	0%	Ghost IC Compatible - Jan	20 days	Mon 12/14/09	Fri 1/8/10		Andrew,Louis	
119	0%	Reimage Other public computer	50 days	Wed 12/30/09	Tue 3/9/10		Jackie Y,Andrew	
122	0%	<b>Team Member's Other Responsibilities</b>	261 days	Wed 7/1/09	Wed 6/30/10			
123	0%	Leadership Group - Adele, Andrew 1%	261 days	Wed 7/1/09	Wed 6/30/10			
124	0%	NetManagers - Steve 1%, Andrew 1%	261 days	Wed 7/1/09	Wed 6/30/10			
125	0%	Docuware UG - Jackie 1%	261 days	Wed 7/1/09	Wed 6/30/10			
126	0%	Library Network - Steve (5%), Bob (1%), Jackie D (1%)	261 days	Wed 7/1/09	Wed 6/30/10			
127	0%	Inventory Nudge - Louis 1%	261 days	Wed 7/1/09	Wed 6/30/10			
128	0%	Peripheral Nudge - Luois 1%	261 days	Wed 7/1/09	Wed 6/30/10			
129	0%	Ntag Nudge - David 1%	261 days	Wed 7/1/09	Wed 6/30/10			
130	0%	Surplusing Nudge - Andrew 1%	261 days	Wed 7/1/09	Wed 6/30/10			
131	0%	Gantt Chart Nudge - Adele 5%	261 days	Wed 7/1/09	Wed 6/30/10			
132	0%	Purchasing - Jackie D, Bob, Steve, Petra, Andrew, David - 3%	261 days	Wed 7/1/09	Wed 6/30/10			
133	0%	Order Parts - Steve 1%, Louis 1% , Andrew 1%	261 days	Wed 7/1/09	Wed 6/30/10			
134	0%	Security Coordinator - Jackie Dee 30%	261 days	Wed 7/1/09	Wed 6/30/10			
135	0%	Student Supervision - Andrew 10%, Louis 10%	261 days	Wed 7/1/09	Wed 6/30/10			
136	0%	CCP Liaison - David 5%	261 days	Wed 7/1/09	Wed 6/30/10			
137	0%	Software Licensing - Jackie YB 20%, Ann 2%	261 days	Wed 7/1/09	Wed 6/30/10			
138	0%	<b>Continuing Work</b>	261 days	Wed 7/1/09	Wed 6/30/10			
139	0%	<b>Server Administration</b>	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Jackie D,Bob	
140	0%	test restores from rsync and backups, database restores for websites	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Jackie D,Bob,Ann	

Project: XWING projects 0910 - Proj 2 Date: Tue 10/13/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	% Complete	Task Name	Duration	Start	Finish	Preced	Resource Names	2nd Q Apr
141	0%	Tape Backups	261 days	Wed 7/1/09	Wed 6/30/10		Louis,Ann,Jackie Y	
142	0%	OS Updates	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Jackie D,Bob	
143	0%	DB Updates	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Jackie D,Bob	
144	0%	Analyze and Clean DB Accounts/Services on Servers	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Jackie D,Bob	
145	0%	Software Updates	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Jackie D,Bob,Ann	
146	<b>0%</b>	<b>Project Management</b>	<b>261 days</b>	<b>Wed 7/1/09</b>	<b>Wed 6/30/10</b>		<b>Adele</b>	
147	0%	Manage Projects	261 days	Wed 7/1/09	Wed 6/30/10		XWING	
148	0%	Specification and Purchase of Equipment	261 days	Wed 7/1/09	Wed 6/30/10		Steve,Bob	
149	<b>0%</b>	<b>Remedy Coordination</b>	<b>261 days</b>	<b>Wed 7/1/09</b>	<b>Wed 6/30/10</b>		<b>XWING</b>	
150	0%	Managing Remedy	261 days	Wed 7/1/09	Wed 6/30/10		Adele,Jackie YB	
151	0%	Helpline Administrator - daily	261 days	Wed 7/1/09	Wed 6/30/10		XWING	
152	<b>0%</b>	<b>Inventory Maintenance</b>	<b>261 days</b>	<b>Wed 7/1/09</b>	<b>Wed 6/30/10</b>		<b>David,Jackie Y</b>	
153	0%	Coordinate w/ Shipping for N-Tags	261 days	Wed 7/1/09	Wed 6/30/10		Jackie Y	
154	0%	Take initial inventory on new equipment & enter (delegate to students)	261 days	Wed 7/1/09	Wed 6/30/10		David,Students	
155	0%	Periodic inventory checks (monthly & as needed)	261 days	Wed 7/1/09	Wed 6/30/10		David,Jackie Y	
156	<b>0%</b>	<b>Preventative Maintenance</b>	<b>261 days</b>	<b>Wed 7/1/09</b>	<b>Wed 6/30/10</b>		<b>XWING</b>	
157	0%	Maintain MAC's daily	261 days	Wed 7/1/09	Wed 6/30/10		Steve,David,Andrew	
158	0%	IC maintenance work	261 days	Wed 7/1/09	Wed 6/30/10		Jackie Y,Andrew	
159	<b>0%</b>	<b>Research and Consulting</b>	<b>261 days</b>	<b>Wed 7/1/09</b>	<b>Wed 6/30/10</b>		<b>XWING</b>	
160	0%	Researching user questions outside of Helpline	261 days	Wed 7/1/09	Wed 6/30/10		XWING	
161	0%	5-year Budget Plan	261 days	Wed 7/1/09	Wed 6/30/10		Adele	


Project: XWING projects 0910 - Proj 2  
Date: Tue 10/13/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

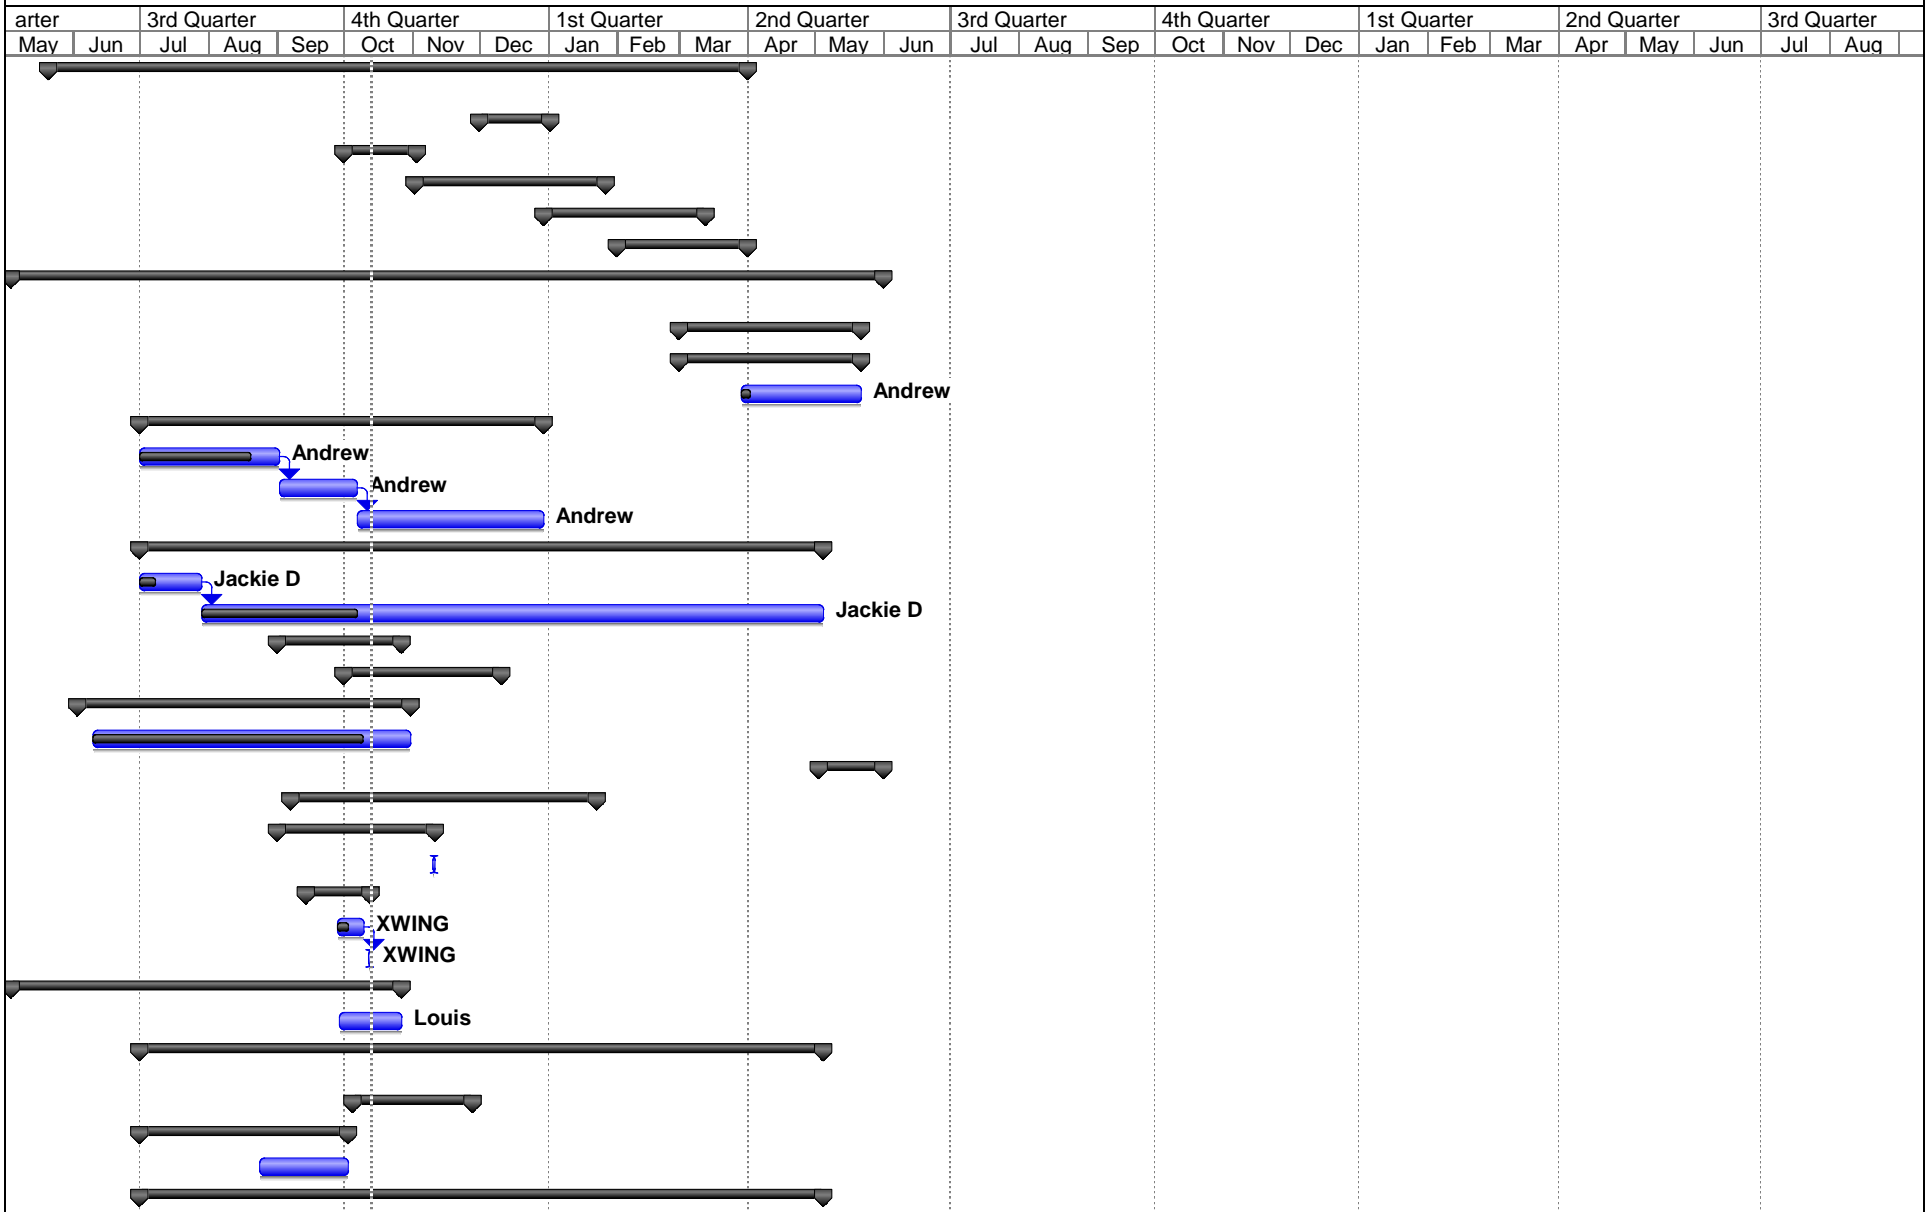

Project: XWING projects 0910 - Proj 2  
Date: Tue 10/13/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

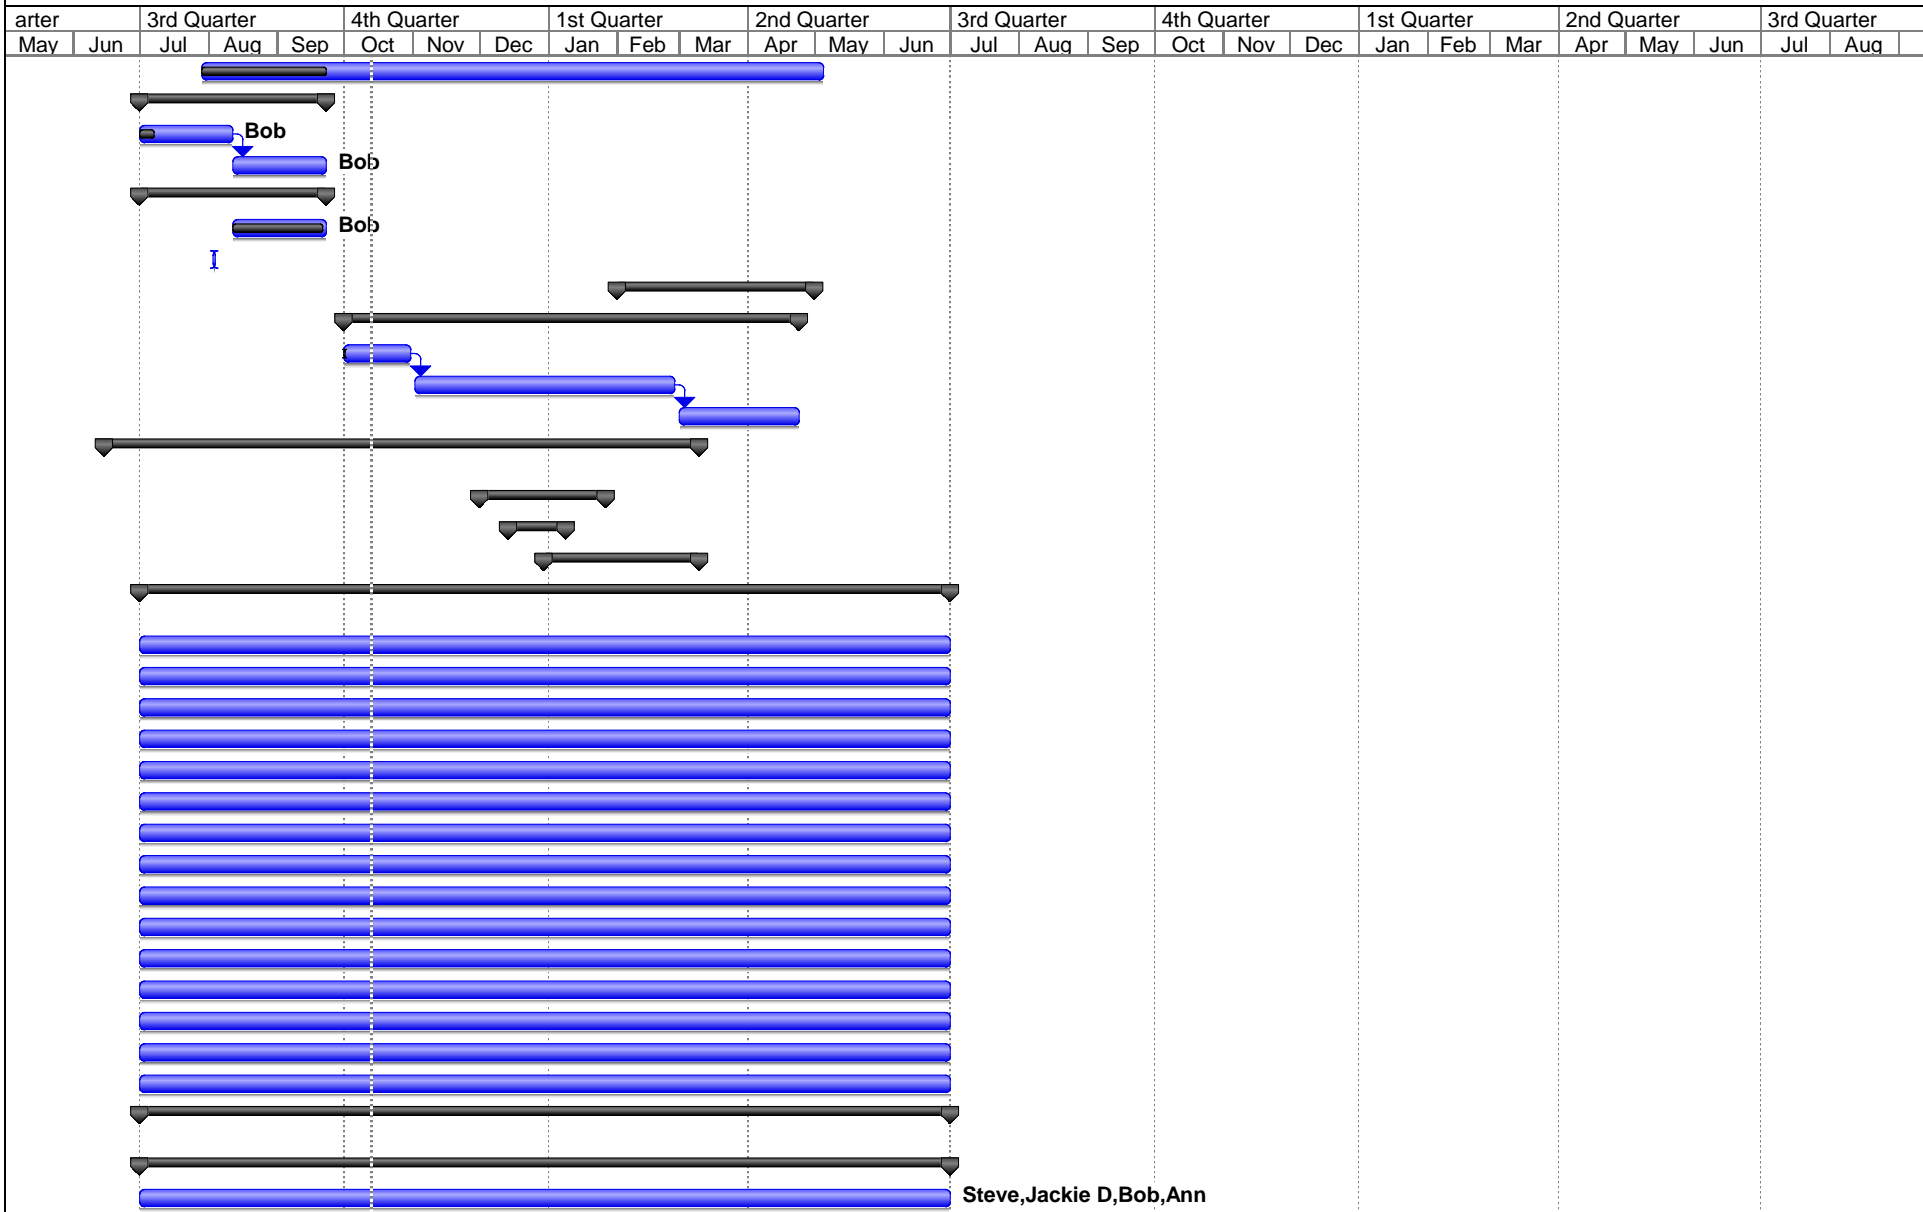

Project: XWING projects 0910 - Proj 2  
Date: Tue 10/13/09

- Task Milestone
- Split Summary
- Progress Project Summary
- External Tasks
- External Milestone
- Deadline

